


Work to begin 7/5/2022

- Work will begin on the East side of the lot
- Lot will be turned over as each section is completed
- Resurfacing of fire lanes will take place on weekends
- Fire lanes will be open to one way traffic during the week

Work to be complete by 7/15/2022

Available Parking During This Time

Phase 1	ADA	Parking
North Lot - North		
North Lot	0	0
South Lot	30	580
Overflow	0	225
WFSC	4	94
WATB	5	96
Temp Lot 2021	0	100
Temp Lot 2022	0	0
<b>Total</b>	<b>39</b>	<b>1095</b>
<b>Total Spaces Available</b>		<b>1134</b>

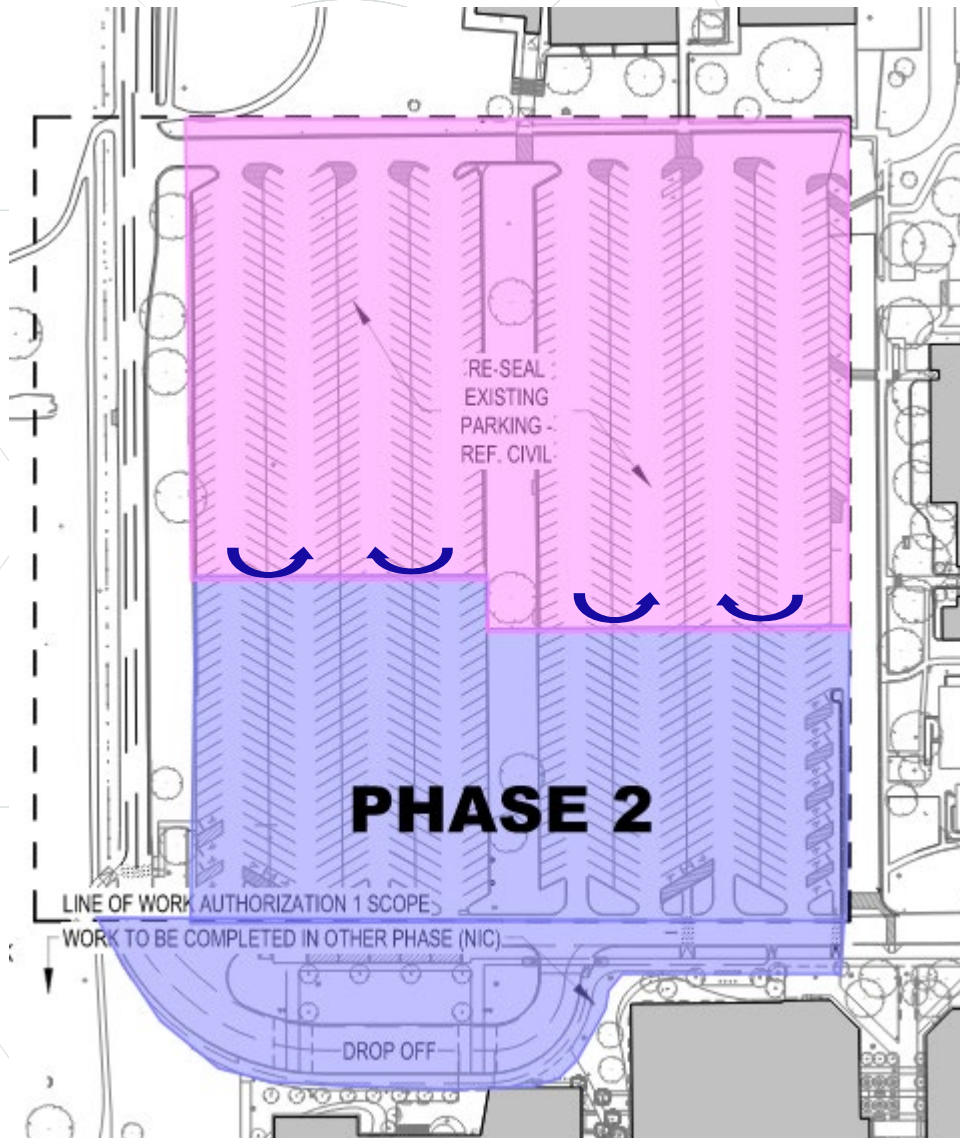


Work to begin 7/5/2022

- This work will begin concurrently with the North Side of the lot
- There will be major earthwork to bring the parking lot grade to the same level as Building 1, with slopes to the accessible parking

Work to be complete by 9/9/2022

Available Parking During This Time

Phase 2 North Lot - South	ADA	Parking
North Lot (After 7/15/22)	6	501
South Lot	30	580
Overflow	0	225
WFSC	4	94
WATB	5	96
Temp Lot 2021	0	100
Temp Lot 2022	0	0
<b>Total</b>	<b>45</b>	<b>1596</b>
<b>Total Spaces Available</b>		<b>1641</b>

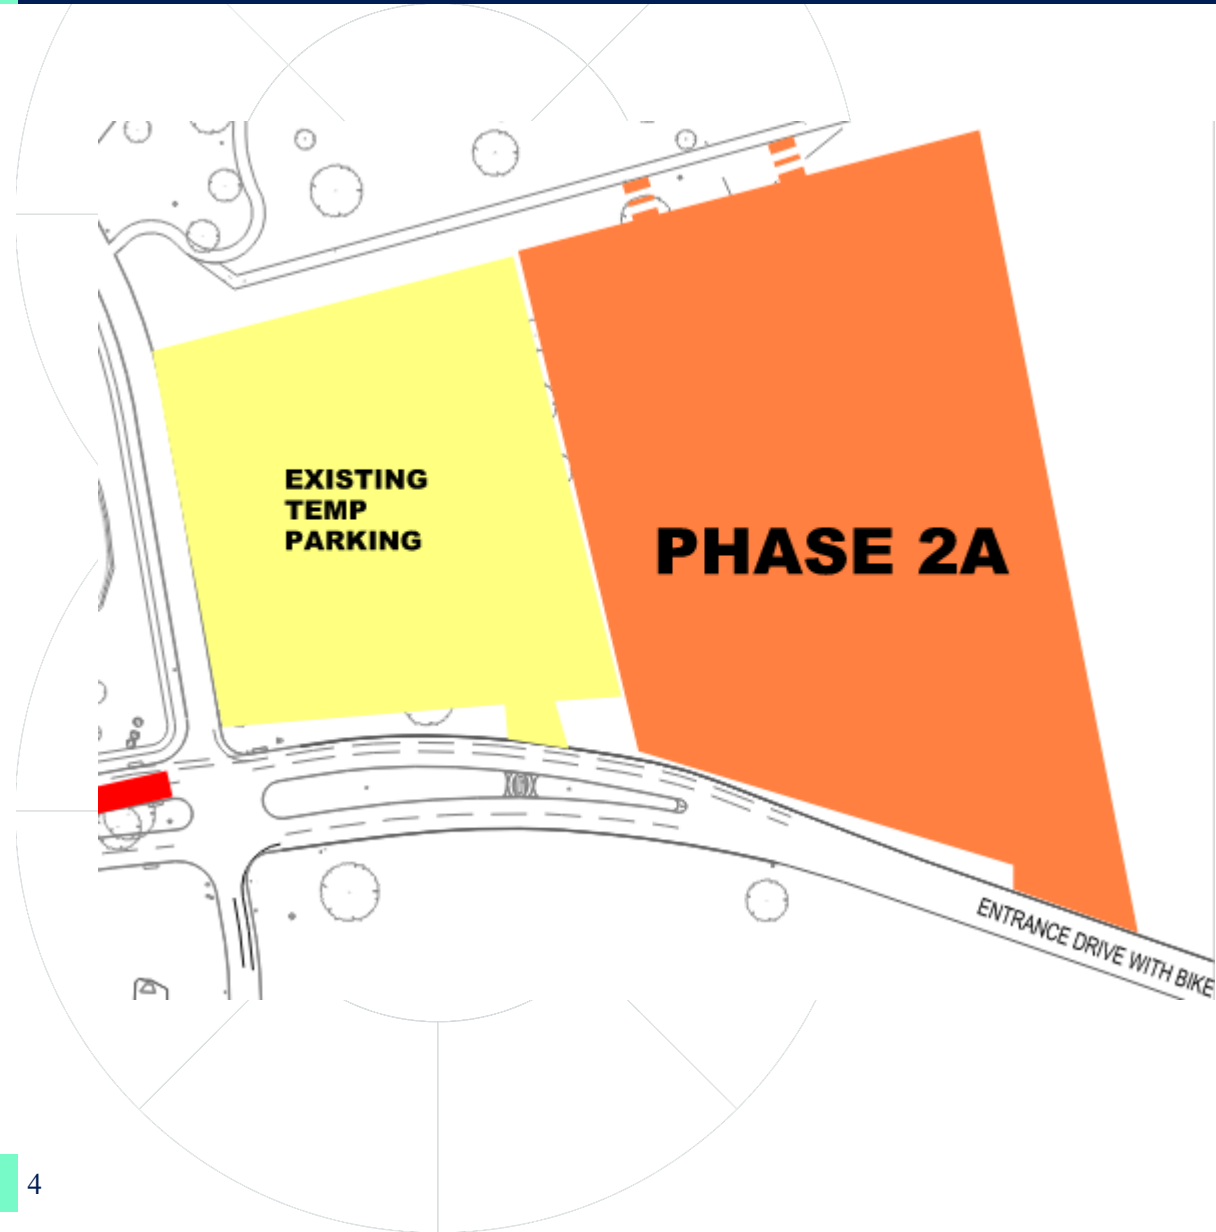


Work to begin 8/15/2022

- Additional 250 vehicle temporary parking
- New curb cut along entrance drive for entry and exit
- Temporary lighting will be installed
- Walkways added to connect to existing sidewalk

Work to be complete by 9/14/2022

\*Parking lot capacity remains the same as Phase 2 while this temporary lot is constructed

# Phase 3– South Lot

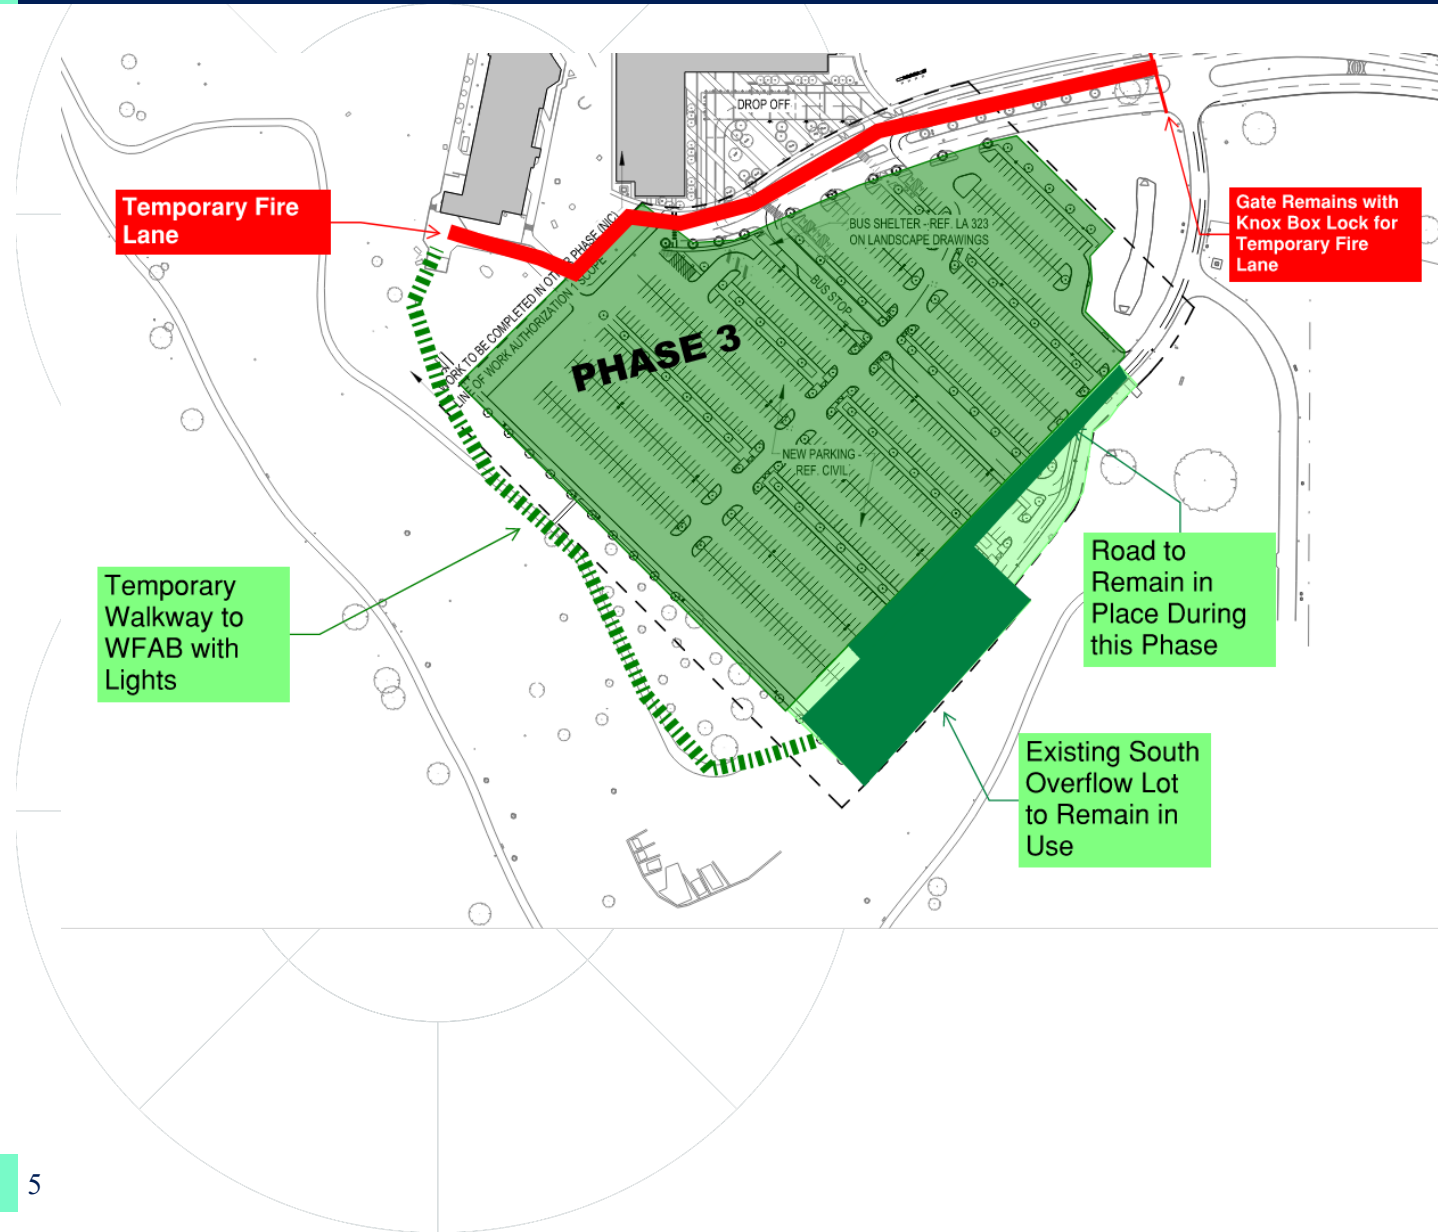

Work to begin 9/19/2022


- Overflow parking at south end of the lot to remain in place for this phase of work
- Temporary walkway to connect from Overflow lot to WFAB with lighting
- Temporary fire lane will be in place for emergency vehicles only

Work to be complete by 1/31/2023

Available Parking During This Time

Phase 3 South Lot	ADA	Parking
North Lot	24	835
South Lot	0	0
Overflow	0	80
WFSC	4	94
WATB	5	96
Temp Lot 2021	0	100
Temp Lot 2022	0	250
<b>Total</b>	<b>33</b>	<b>1455</b>
<b>Total Spaces Available</b>		<b>1488</b>

# Phase 4– South Overflow Lot

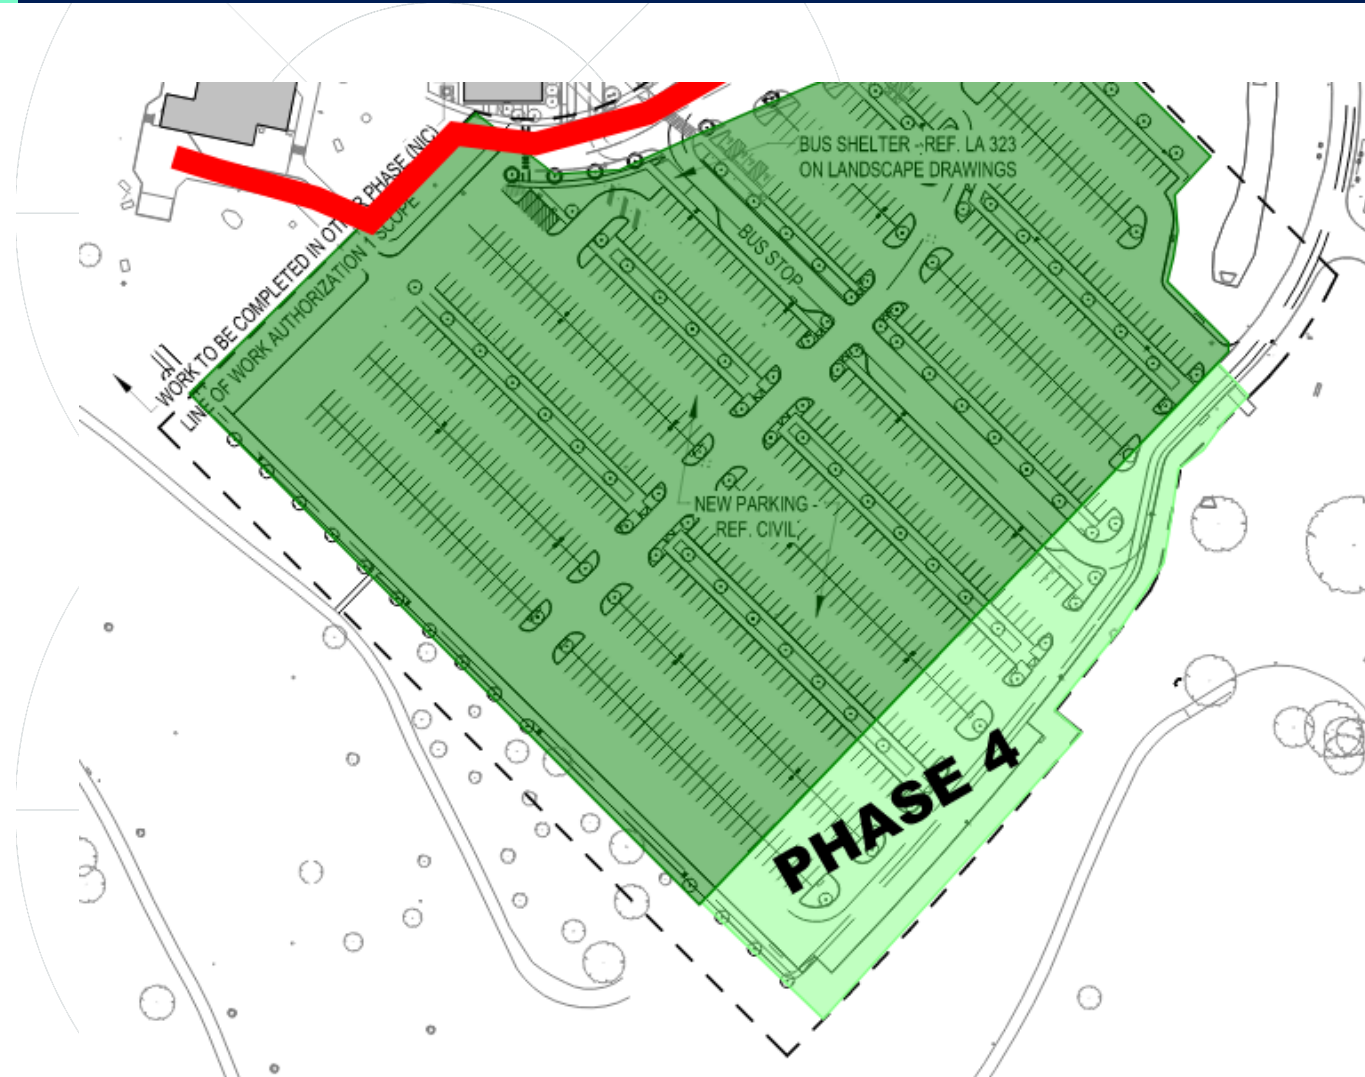

Work to begin 2/1/2023

- This work will incorporate the existing overflow parking to the south into the lot
- Landscaping work for the entire South lot will be completed during this time

Work to be complete by 6/20/2023

Available Parking During This Time

Phase 4 South Overflow Lot	ADA	Parking
North Lot	24	835
South Lot	21	841
Overflow	0	0
WFSC	4	94
WATB	5	96
Temp Lot 2021	0	100
Temp Lot 2022	0	250
<b>Total</b>	<b>54</b>	<b>2216</b>
<b>Total Spaces Available</b>		<b>2270</b>

# Parking Count at Completion



- Temporary Lots will be removed when work is complete in 6/2023
- All campus parking will be paved
- Additional 11 spaces available at completion

At Completion	ADA	Parking
North Lot	24	835
South Lot	21	968
Overflow	0	0
WFSC	4	94
WATB	5	96
Temp Lot 2021	0	0
Temp Lot 2022	0	0
Total	54	1993
Total Spaces Available		2047
